




SR166 MP 4.52 OLNEY CREEK  
15.0201 0.90  
CROSSING E

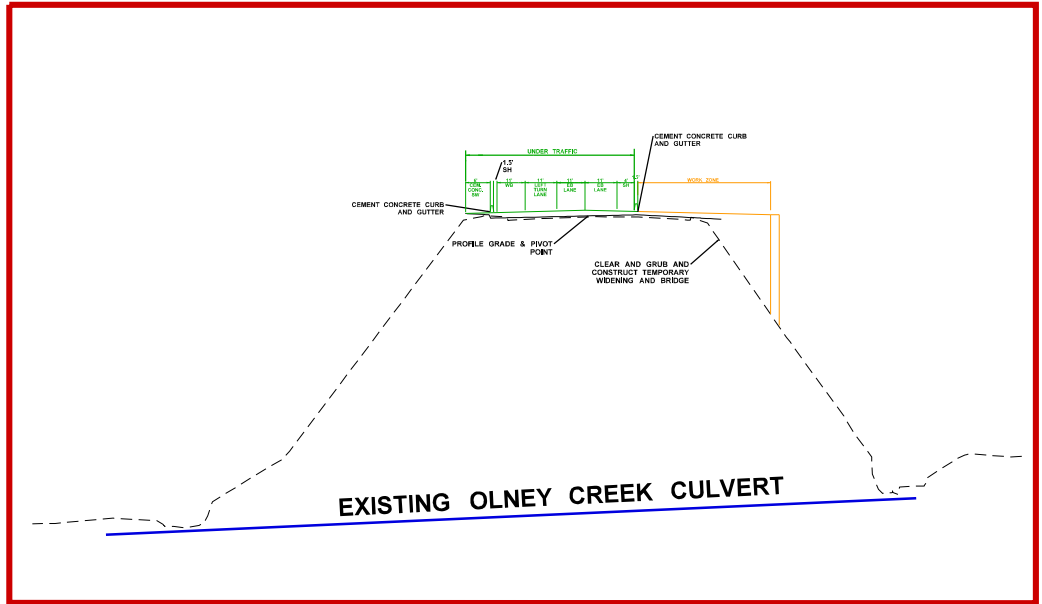


MOT STAGE 1

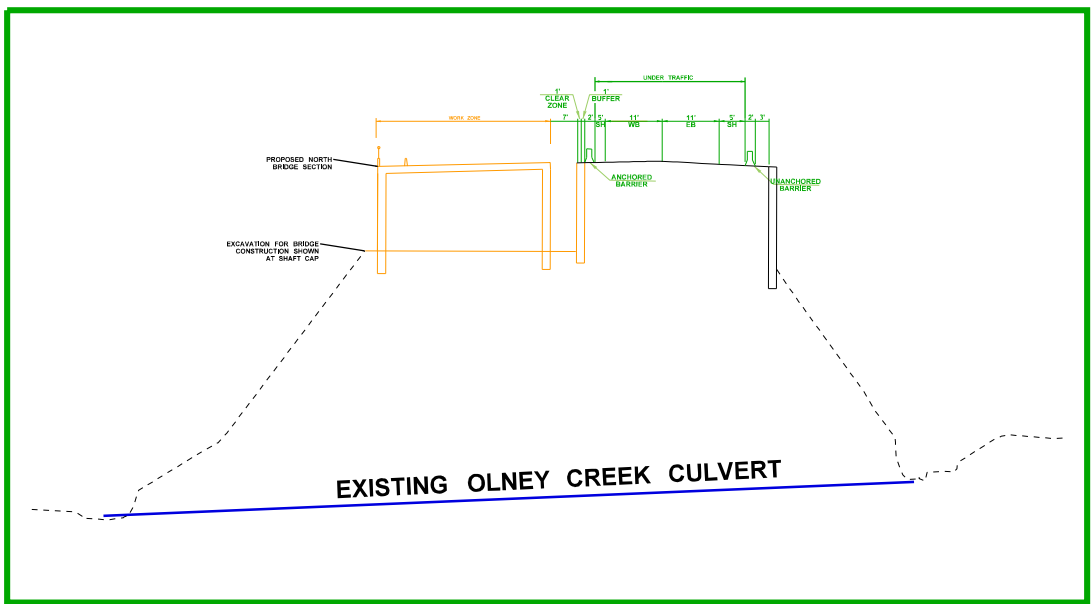


MOT STAGE 2

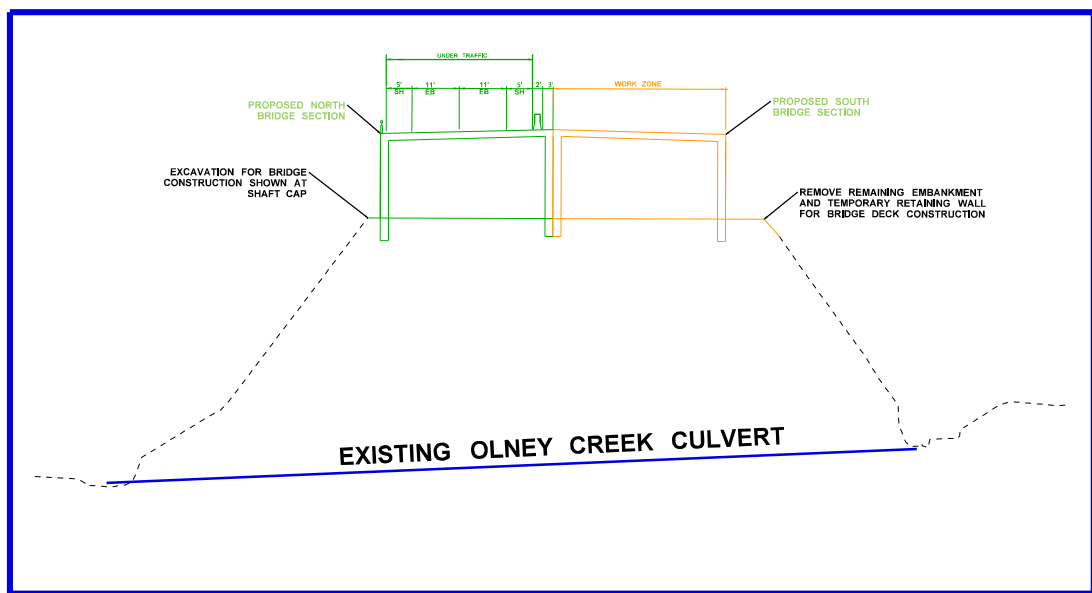


MOT STAGE 3

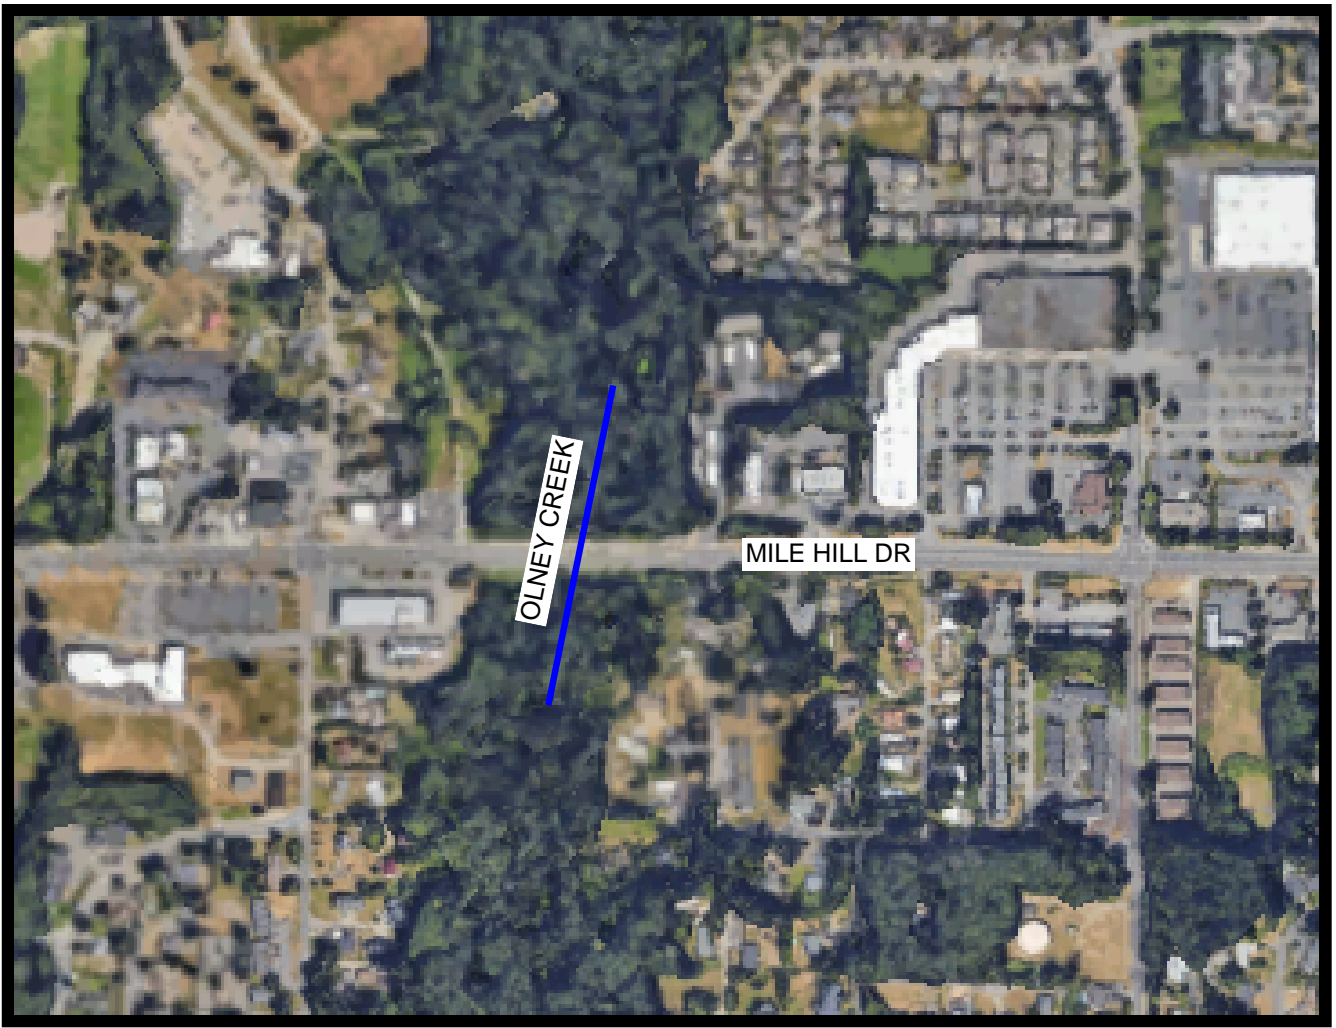

VICINITY MAP

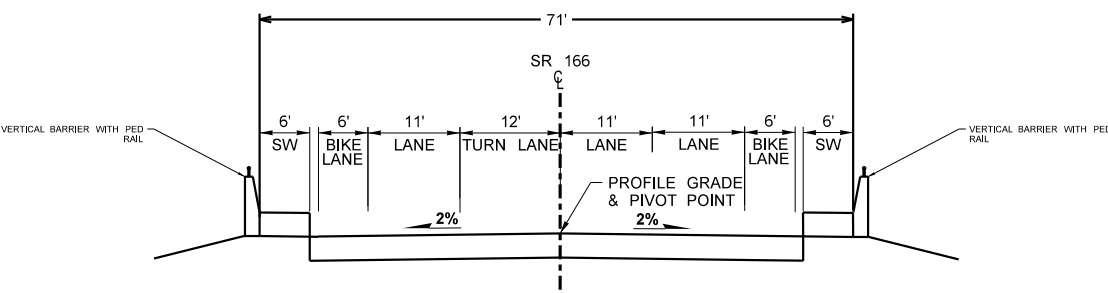

BRIDGE TYPICAL SECTION

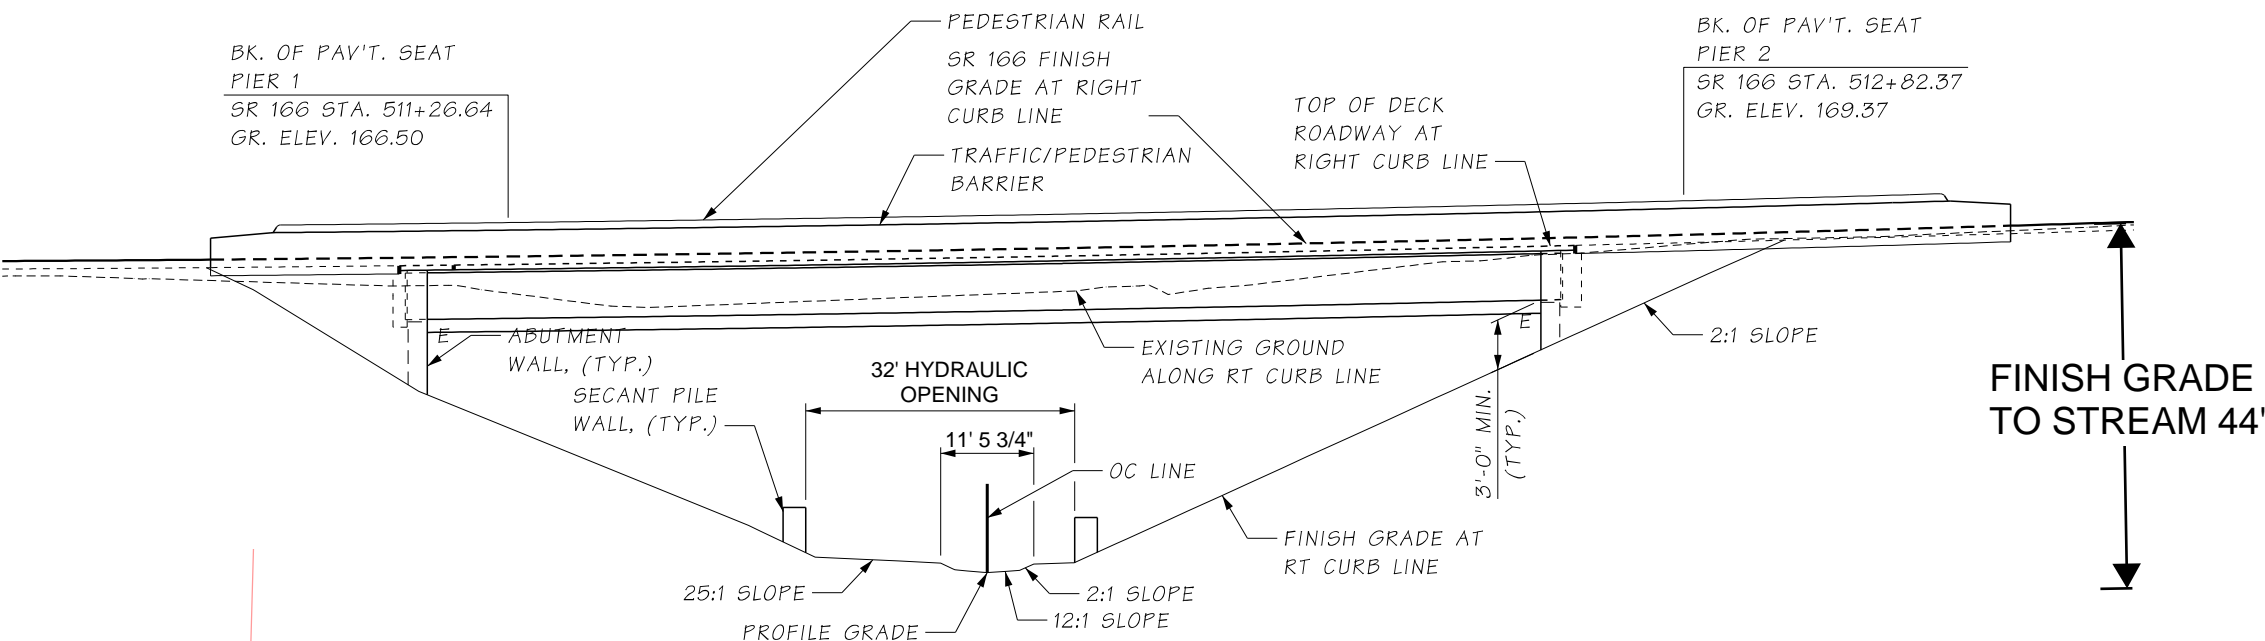

BRIDGE ELEVATION VIEW

MOT STAGE 1 CONSTRUCTION (3 MONTHS)

1. ESTABLISH BARRIER PROTECTED WORK AREA
2. CLEAR AND GRUB AND CONSTRUCT EB TEMPORARY WIDENING
3. CONSTRUCT TEMPORARY WIDENING AND TEMPORARY BRIDGE

MOT STAGE 2 CONSTRUCTION (6 MONTHS)


1. SHIFT TRAFFIC
2. ESTABLISH PROTECTED WORK AREA
3. TEMPORARILY REALIGN DRIVEWAYS
4. CONSTRUCT PROPOSED NORTH SECTION OF BRIDGE

MOT STAGE 3 CONSTRUCTION (8 MONTHS)

1. SHIFT TRAFFIC ONTO PERMANENT BRIDGE AND ESTABLISH PROTECTED WORK AREA
2. REMOVE SOUTH MOT LANES AND EXISTING EMBANKMENT
3. CONSTRUCT SOUTH SIDE OF BRIDGE

MOT STAGE 4 CONSTRUCTION (3 MONTHS)

1. STREAM RESTORATION
2. ROADSIDE RESTORATION

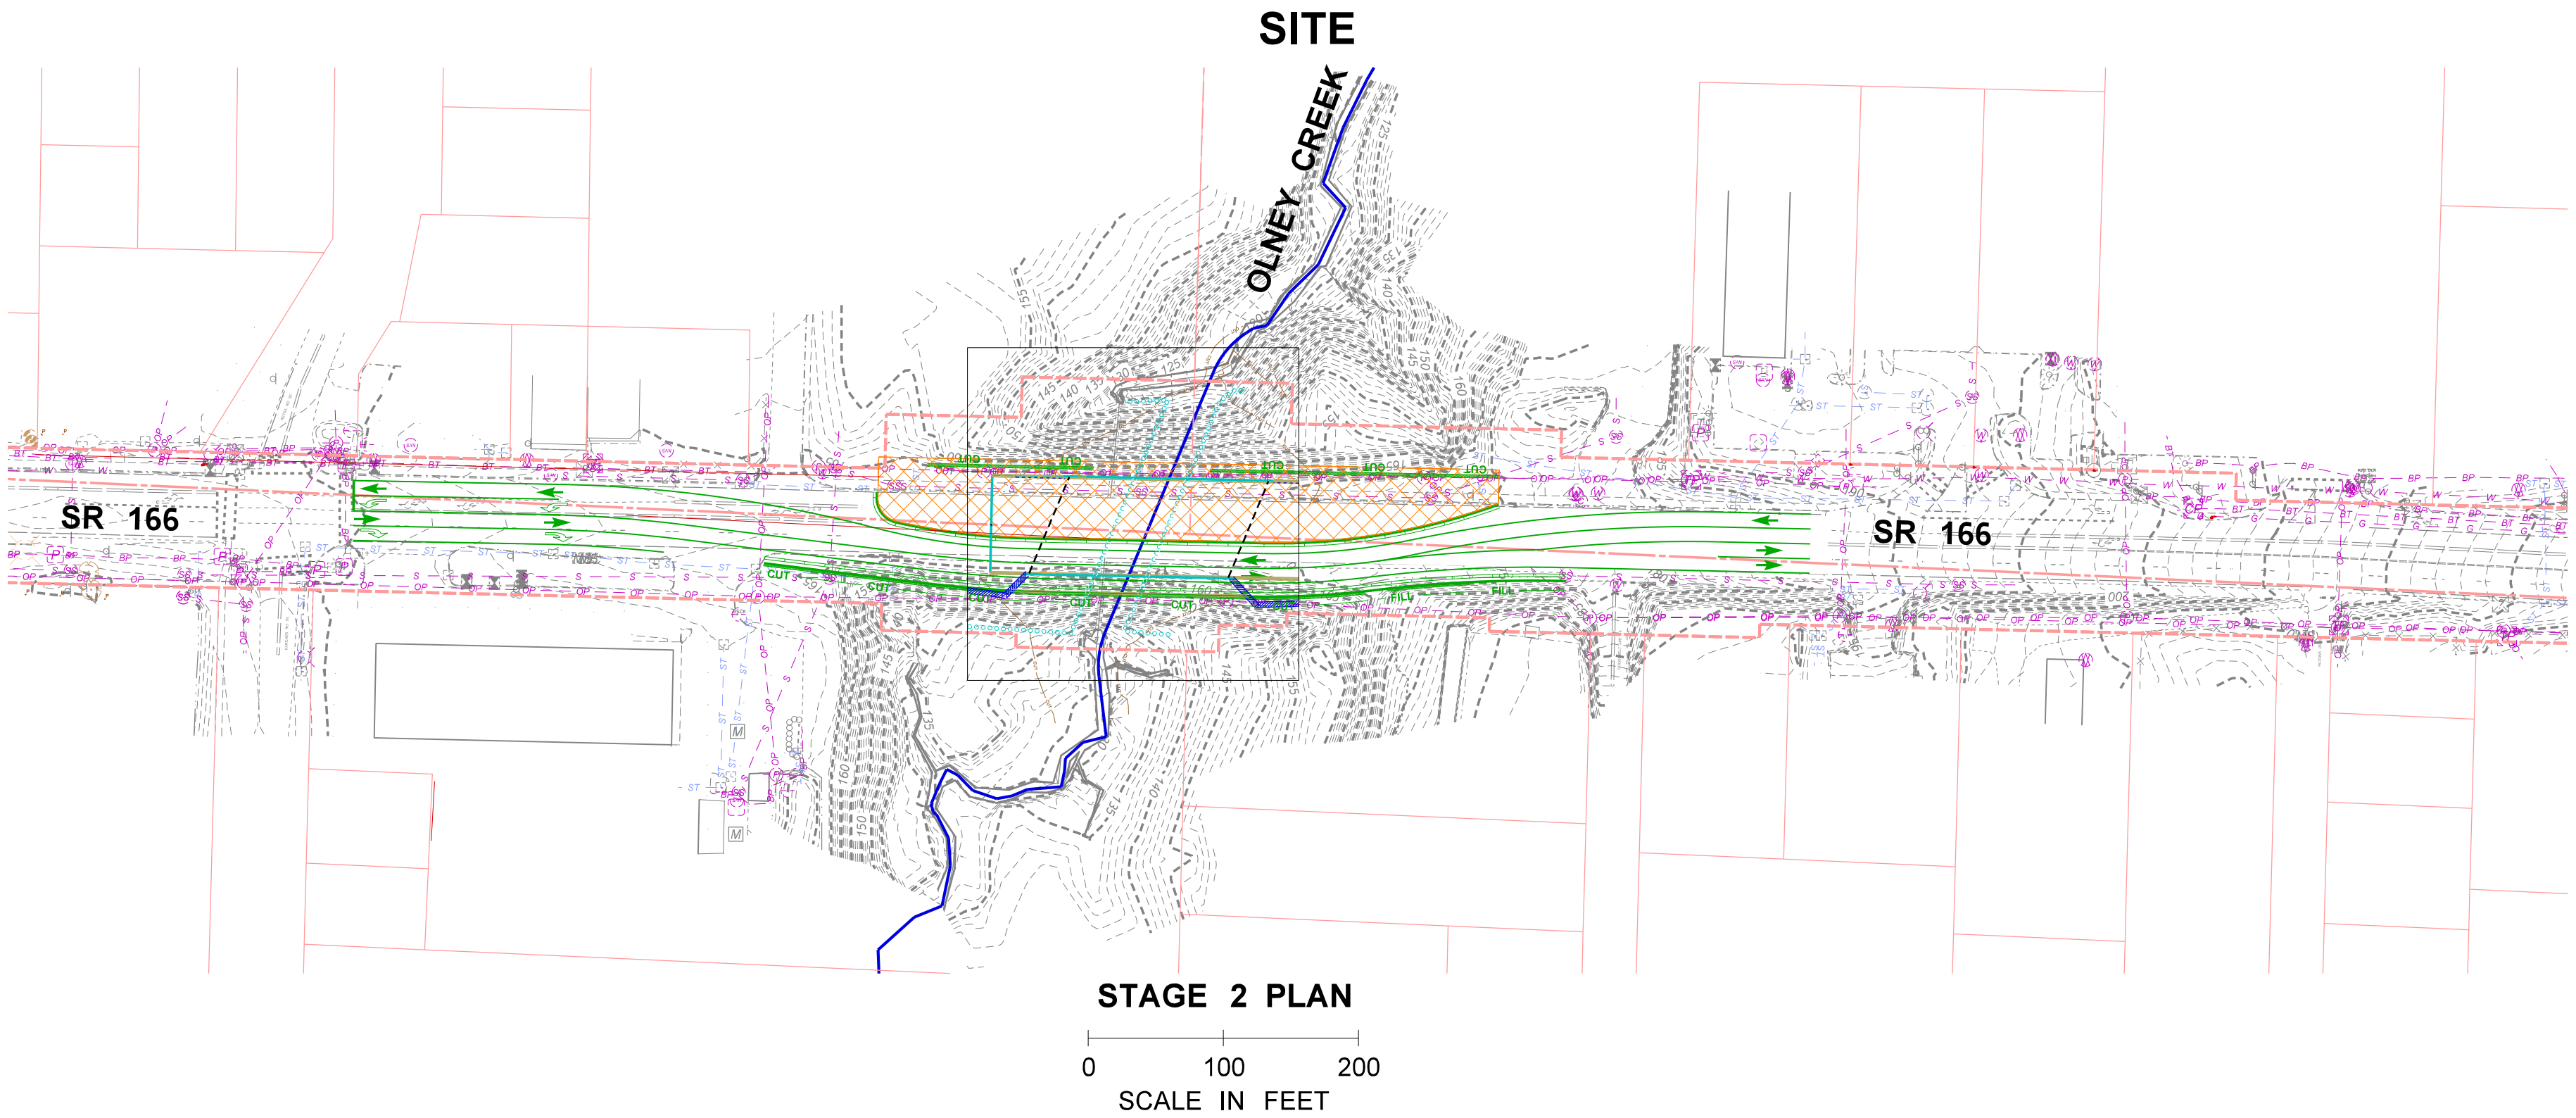

STAGE 2 PLAN

0 100 200  
SCALE IN FEET

LEGEND	
	STAGE 2 TRAFFIC ALIGNMENT
	CONSTRUCTED BRIDGE AND SLOT WALLS
	RIGHT-OF-WAY AND PARCEL LINES
	WORK ZONE
	PROPOSED STREAM

FILE NAME c:\users\vassemar\pw\_wsdot\0587269\Crossing E Roll Plot.dgn

TIME 1:08:11 PM

DATE 9/25/2023

PLOTTED BY vassemar

DESIGNED BY

ENTERED BY

CHECKED BY

PROJ. ENGR.

REGIONAL ADM.

REVISION

DATE

BY

REGION NO.

STATE

10

WASH

JOB NUMBER

CONTRACT NO.

FED.AID PROJ.NO.

LOCATION NO.

P.E. STAMP BOX

P.E. STAMP BOX



SR 3 / SR16 / SR166  
GORST VICINITY -  
REMOVE FISH BARRIERS

CROSSING E - CONCEPT PLAN MOT

PLAN REF NO

SHEET

OF

SHEETS
