
























































Page 1



WSDOT SR 526 Corridor Improvements
Phase 2a Preliminary Schedule Geometric Design
September 22, 2020

ID	Task Name	Duration	Start	Finish	Predecessors	Late Start	Late Finish												
								Sep	Qtr 4, 2021	Oct	Nov	Dec	2022 Qtr 1, 2022	Jan	Feb				
108	QC of Draft Preliminary Structures Plans	5 days	Mon 11/15/21	Fri 11/19/21	107	Wed 12/15/21	Tue 12/21/21												
109	Address QC Comments	5 days	Mon 11/22/21	Fri 11/26/21	108	Wed 12/22/21	Tue 12/28/21												
110	WSDOT Review of Preliminary Structures Plans	10 days	Mon 11/29/21	Fri 12/10/21	109	Wed 12/29/21	Tue 1/11/22												
111	Address WSDOT Comments	5 days	Mon 12/13/21	Fri 12/17/21	110	Wed 1/12/22	Tue 1/18/22												
112	11.2 Preliminary Plans Preparation	100 days	Mon 9/13/21	Fri 1/28/22		Wed 9/22/21	Tue 12/20/22												
113	11.2.1 Preliminary Plans Preparation	100 days	Mon 9/13/21	Fri 1/28/22		Wed 9/22/21	Tue 12/20/22												
114	Prepare Plans (30%)	100 days	Mon 9/13/21	Fri 1/28/22		Wed 9/22/21	Tue 12/20/22												
115	Index & Vicinity Map	10 days	Mon 9/13/21	Fri 9/24/21	2	Wed 11/10/21	Tue 11/23/21												
116	Roadway Sections	20 days	Mon 10/18/21	Fri 11/12/21	76FF,75	Wed 10/27/21	Tue 11/23/21												
117	Alignment/RW Plans	20 days	Mon 10/18/21	Fri 11/12/21	76FF,75	Wed 10/27/21	Tue 11/23/21												
118	Temp Construction Easements	40 days	Mon 12/6/21	Fri 1/28/22	55	Wed 10/26/22	Tue 12/20/22												
119	Utility Plans	20 days	Mon 9/13/21	Fri 10/8/21	2	Wed 10/27/21	Tue 11/23/21												
120	TESC Plans	30 days	Wed 9/22/21	Tue 11/2/21	75	Wed 10/13/21	Tue 11/23/21												
121	Conceptual Drainage Plans	20 days	Mon 9/13/21	Fri 10/8/21	2	Wed 11/10/21	Tue 12/7/21												
122	Paving Plans	45 days	Wed 9/22/21	Tue 11/23/21	75	Wed 9/22/21	Tue 11/23/21												
123	Pavement Marking Plans	25 days	Wed 9/22/21	Tue 10/26/21	75	Wed 10/20/21	Tue 11/23/21												
124	Bridge and Structures Plans	35 days	Mon 10/4/21	Fri 11/19/21	107SS	Wed 10/6/21	Tue 11/23/21												
125	QC of Draft Preliminary Plans	5 days	Wed 11/24/21	Tue 11/30/21	115,116,117,119,120,124,123,12	Wed 11/24/21	Tue 11/30/21												
126	Address QC Comments	5 days	Wed 12/1/21	Tue 12/7/21	125	Wed 12/1/21	Tue 12/7/21												
127	WSDOT Review	20 days	Wed 12/8/21	Tue 1/4/22	126,121	Wed 12/8/21	Tue 1/4/22												
128	Address WSDOT Comments	10 days	Wed 1/5/22	Tue 1/18/22	127,111FF	Wed 1/5/22	Tue 1/18/22												
129	11.2.2 Preliminary Engineers Cost Estimate	39 days	Mon 11/15/21	Thu 1/6/22		Thu 4/14/22	Tue 6/7/22												
130	Develop Draft Preliminary Engineers Cost Estimate	20 days	Mon 11/15/21	Fri 12/10/21	117	Thu 4/14/22	Wed 5/11/22												
131	QC of Draft Preliminary Engineers Cost Estimate	5 days	Mon 12/13/21	Fri 12/17/21	130	Thu 5/12/22	Wed 5/18/22												
132	Address QC Comments	4 days	Mon 12/20/21	Thu 12/23/21	131	Thu 5/19/22	Tue 5/24/22												
133	WSDOT Review of Preliminary Engineers Cost Estimate	10 days	Fri 12/24/21	Thu 1/6/22	132	Wed 5/25/22	Tue 6/7/22												
134	11.3 Hydraulics Report	210 days	Mon 9/13/21	Fri 7/1/22		Wed 3/2/22	Tue 12/20/22												
135	Draft Hydraulics Report	60 days	Mon 9/13/21	Fri 12/3/21	2	Wed 3/2/22	Tue 5/24/22												
136	WSDOT Review of Draft Hydraulics Report	10 days	Mon 12/6/21	Fri 12/17/21	135	Wed 5/25/22	Tue 6/7/22												
137	Address WSDOT Comments	20 days	Mon 12/20/21	Fri 1/14/22	136	Wed 6/8/22	Tue 7/5/22												
138	Final Design	40 days	Mon 1/17/22	Fri 3/11/22	137	Wed 7/6/22	Tue 8/30/22												
139	Final Hydraulics Report	60 days	Mon 3/14/22	Fri 6/3/22	138	Wed 8/31/22	Tue 11/22/22												
140	WSDOT Review of Final Hydraulics Report	10 days	Mon 6/6/22	Fri 6/17/22	139	Wed 11/23/22	Tue 12/6/22												
141	Address WSDOT Comments	10 days	Mon 6/20/22	Fri 7/1/22	140	Wed 12/7/22	Tue 12/20/22												
142	11.4 Traffic Management Plan	85 days	Mon 10/11/21	Fri 2/4/22		Wed 8/24/22	Tue 12/20/22												
143	Prepare Draft TMP	25 days	Mon 10/11/21	Fri 11/12/21	2FS+20 days	Wed 8/24/22	Tue 9/27/22												
144	QC/Review of Draft TMP	5 days	Mon 11/15/21	Fri 11/19/21	143	Wed 9/28/22	Tue 10/4/22												
145	Address QC/Review Comments	5 days	Mon 11/22/21	Fri 11/26/21	144	Wed 10/5/22	Tue 10/11/22												
146	WSDOT Review of Draft TMP	10 days	Mon 11/29/21	Fri 12/10/21	145	Wed 10/12/22	Tue 10/25/22												
147	Address WSDOT Comment	10 days	Mon 12/13/21	Fri 12/24/21	146	Wed 10/26/22	Tue 11/8/22												
148	Prepare Final TMP	20 days	Mon 12/27/21	Fri 1/21/22	147	Wed 11/9/22	Tue 12/6/22												
149	QC/Review of Final TMP	5 days	Mon 1/24/22	Fri 1/28/22	148	Wed 12/7/22	Tue 12/13/22												
150	Address QC/Review Comments	5 days	Mon 1/31/22	Fri 2/4/22	149	Wed 12/14/22	Tue 12/20/22												
151	Submit Final TMP	0 days	Fri 2/4/22	Fri 2/4/22	150	Tue 12/20/22	Tue 12/20/22												
152	11 Cost Risk and VE (WSDOT Lead)	24 days	Tue 1/4/22	Fri 2/4/22		Tue 1/4/22	Fri 2/4/22												
153	CRA Workshop	2 days	Tue 1/4/22	Wed 1/5/22		Mon 12/19/22	Tue 12/20/22												
154	VE Workshop	4 days	Tue 2/1/22	Fri 2/4/22		Thu 12/15/22	Tue 12/20/22												
155	12.0 Plans, Specifications & Estimate	248 days	Fri 1/7/22	Tue 12/20/22		Wed 1/19/22	Tue 12/20/22												
156	12.1 Contracts Plans Preparation	240 days	Wed 1/19/22	Tue 12/20/22		Wed 1/19/22	Tue 12/20/22												
157	60% Plans Development	80 days	Wed 1/19/22	Tue 5/10/22		Wed 1/19/22	Tue 5/10/22												
158	General Sheets	15 days	Wed 1/19/22	Tue 2/8/22	128	Wed 2/9/22	Tue 3/1/22												
159	Roadway Sections	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 2/2/22	Tue 3/1/22												
160	Stage Construction Plans	15 days	Wed 1/19/22	Tue 2/8/22	128	Wed 2/9/22	Tue 3/1/22												
161	Alignment & RW Plans	10 days	Wed 1/19/22	Tue 2/1/22	128	Wed 2/16/22	Tue 3/1/22												
162	Site Preparation Plans	15 days	Wed 1/19/22	Tue 2/8/22	128	Wed 2/9/22	Tue 3/1/22												


























































<p>WSDOT SR 526 Corridor Improvements Phase 2a Preliminary Schedule Geometric Design September 22, 2020</p>									
---	--	--	--	--	--	--	--	--	--

Task Name	Mod	Duration	Start	Finish	Predecessors	Late Start	Late Finish	2022						
								Qtr 4, 2021		Qtr 1, 2022				
								Sep	Oct	Nov	Dec			
								Jan				Feb		
163		Drainage Plans	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 2/2/22	Tue 3/1/22						
164		Existing Utility Plans	10 days	Wed 1/19/22	Tue 2/1/22	128	Wed 2/16/22	Tue 3/1/22						
165		TESC Plans	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 2/2/22	Tue 3/1/22						
166		Landscape and Roadside Restoration Plans - WSDOT	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 3/2/22	Tue 3/29/22						
167		Paving Plans	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 2/2/22	Tue 3/1/22						
168		Pavement Marking Plans	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 2/2/22	Tue 3/1/22						
169		Traffic Plans - WSDOT	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 3/2/22	Tue 3/29/22						
170		Bridge and Structures Plans	30 days	Wed 1/19/22	Tue 3/1/22	128	Wed 1/19/22	Tue 3/1/22						
171		Traffic Control Plans	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 2/2/22	Tue 3/1/22						
172		QC of 60% Plans	10 days	Wed 3/2/22	Tue 3/15/22	158,159,160,161,162,163,164,165	Wed 3/2/22	Tue 3/15/22						
173		Address QC Comments	10 days	Wed 3/16/22	Tue 3/29/22	172	Wed 3/16/22	Tue 3/29/22						
174		WSDOT Review of 60% Plans	20 days	Wed 3/30/22	Tue 4/26/22	173,169,166	Wed 3/30/22	Tue 4/26/22						
175		Address WSDOT Comments	10 days	Wed 4/27/22	Tue 5/10/22	174	Wed 4/27/22	Tue 5/10/22						
176		90% Plans Development	105 days	Wed 5/11/22	Tue 10/4/22		Wed 5/11/22	Tue 12/20/22						
177		General Sheets	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
178		Roadway Sections	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
179		Stage Construction Plans	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
180		Alignment & RW Plans	5 days	Wed 5/11/22	Tue 5/17/22	175	Wed 6/1/22	Tue 6/7/22						
181		Site Preparation Plans	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
182		Drainage Plans	20 days	Wed 5/11/22	Tue 6/7/22	175	Wed 5/11/22	Tue 6/7/22						
183		Existing Utility Plans	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
184		TESC Plans	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
185		Landscape and Roadside Restoration Plans - WSDOT	20 days	Wed 5/11/22	Tue 6/7/22	175	Wed 11/23/22	Tue 12/20/22						
186		Paving Plans	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
187		Pavement Marking Plans	10 days	Wed 5/11/22	Tue 5/24/22	175	Wed 5/25/22	Tue 6/7/22						
188		Traffic Plans - WSDOT	20 days	Wed 5/11/22	Tue 6/7/22	175	Wed 11/23/22	Tue 12/20/22						
189		Bridge and Structures Plans	20 days	Wed 5/11/22	Tue 6/7/22	175	Wed 5/11/22	Tue 6/7/22						
190		Traffic Control Plans	15 days	Wed 5/11/22	Tue 5/31/22	175	Wed 5/18/22	Tue 6/7/22						
191		QC of 90% Plans	5 days	Wed 6/8/22	Tue 6/14/22	177,178,179,180,181,182,183,184	Wed 6/8/22	Tue 6/14/22						
192		Address QC Comments	10 days	Wed 6/15/22	Tue 6/28/22	191	Wed 6/15/22	Tue 6/28/22						
193		WSDOT Review of 90% Plans	60 days	Wed 6/29/22	Tue 9/20/22	192	Wed 6/29/22	Tue 9/20/22						
194		Address WSDOT Comments	10 days	Wed 9/21/22	Tue 10/4/22	193	Wed 9/21/22	Tue 10/4/22						
195		100% Plans Development	55 days	Wed 10/5/22	Tue 12/20/22		Wed 10/5/22	Tue 12/20/22						
196		General Sheets	10 days	Wed 10/5/22	Tue 10/18/22	194	Wed 10/19/22	Tue 11/1/22						
197		Roadway Sections	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
198		Stage Construction Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
199		Alignment & RW Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
200		Site Preparation Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
201		Drainage Plans	20 days	Wed 10/5/22	Tue 11/1/22	194	Wed 10/5/22	Tue 11/1/22						
202		Existing Utility Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
203		TESC Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
204		Landscape and Roadside Restoration Plans - WSDOT	10 days	Wed 10/5/22	Tue 10/18/22	194	Wed 10/19/22	Tue 11/1/22						
205		Paving Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
206		Pavement Marking Plans	5 days	Wed 10/5/22	Tue 10/11/22	194	Wed 10/26/22	Tue 11/1/22						
207		Traffic Plans - WSDOT	10 days	Wed 10/5/22	Tue 10/18/22	194	Wed 10/19/22	Tue 11/1/22						
208		Bridge and Structures Plans	10 days	Wed 10/5/22	Tue 10/18/22	194	Wed 10/19/22	Tue 11/1/22						
209		Traffic Control Plans	10 days	Wed 10/5/22	Tue 10/18/22	194	Wed 10/19/22	Tue 11/1/22						
210		QC of 100% Plans	5 days	Wed 11/2/22	Tue 11/8/22	196,197,198,199,200,201,202,203	Wed 11/2/22	Tue 11/8/22						
211		Address QC Comments	10 days	Wed 11/9/22	Tue 11/22/22	210	Wed 11/9/22	Tue 11/22/22						
212		WSDOT Review of 100% Plans	10 days	Wed 11/23/22	Tue 12/6/22	211	Wed 11/23/22	Tue 12/6/22						
213		Address WSDOT Comments	10 days	Wed 12/7/22	Tue 12/20/22	212	Wed 12/7/22	Tue 12/20/22						
214		Submit Proof Copy	0 days	Tue 12/20/22	Tue 12/20/22	213	Tue 12/20/22	Tue 12/20/22						
215		12.2 Contract Specification Development	228 days	Fri 1/7/22	Tue 11/22/22		Wed 6/8/22	Tue 12/20/22						
216		12.2.1 General Special Provisions	60 days	Wed 1/19/22	Tue 4/12/22		Wed 9/28/22	Tue 12/20/22						
217		Prepare Draft GSP	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 9/28/22	Tue 10/25/22						


Project: SR 526 Phase 2 Schedu
Date: Wed 12/29/21

Task		Summary		Inactive Milestone		Duration-only		Start-only		External Milestone		Critical Split		Progress
Split		Project Summary		Inactive Summary		Manual Summary Rollup		Finish-only		Deadline		Manual Progress		Manual Task
Milestone		Inactive Task		Manual Task		Manual Summary		External Tasks		Critical		Manual Progress		Manual Task

WSDOT SR 526 Corridor Improvements
Phase 2a Preliminary Schedule Geometric Design
September 22, 2020

Task No.	Task Name	Duration	Start	Finish	Predecessors	Late Start	Late Finish					2022		
								Sep	Qtr 4, 2021	Oct	Nov	Dec	Qtr 1, 2022	
													Jan	Feb
218	 QC Draft GSP	5 days	Wed 2/16/22	Tue 2/22/22	217	Wed 10/26/22	Tue 11/1/22							
219	 Address QC Comments	10 days	Wed 2/23/22	Tue 3/8/22	218	Wed 11/2/22	Tue 11/15/22							
220	 WSDOT Review of GSP	20 days	Wed 3/9/22	Tue 4/5/22	219	Wed 11/16/22	Tue 12/13/22							
221	 Address WSDOT Comments	5 days	Wed 4/6/22	Tue 4/12/22	220	Wed 12/14/22	Tue 12/20/22							
222	 12.2.2 Special Provisions	220 days	Wed 1/19/22	Tue 11/22/22		Wed 6/15/22	Tue 12/20/22							
223	 Prepare Draft 60% Special Provisions	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 6/15/22	Tue 7/12/22							
224	 QC Draft 60% Special Provisions	5 days	Wed 2/16/22	Tue 2/22/22	223	Wed 7/13/22	Tue 7/19/22							
225	 Address QC Comments	5 days	Wed 2/23/22	Tue 3/1/22	224	Wed 7/20/22	Tue 7/26/22							
226	 WSDOT Review	20 days	Wed 3/2/22	Tue 3/29/22	225	Wed 7/27/22	Tue 8/23/22							
227	 Address WSDOT Comments	10 days	Wed 3/30/22	Tue 4/12/22	226	Wed 8/24/22	Tue 9/6/22							
228	 Prepare Draft 90% Special Provisions	10 days	Wed 5/11/22	Tue 5/24/22	227,175	Wed 9/7/22	Tue 9/20/22							
229	 QC Draft 90% Special Provisions	5 days	Wed 5/25/22	Tue 5/31/22	228	Wed 9/21/22	Tue 9/27/22							
230	 Address QC Comments	5 days	Wed 6/1/22	Tue 6/7/22	229	Wed 9/28/22	Tue 10/4/22							
231	 WSDOT Review	10 days	Wed 6/8/22	Tue 6/21/22	230	Wed 10/5/22	Tue 10/18/22							
232	 Address WSDOT Comments	10 days	Wed 6/22/22	Tue 7/5/22	231	Wed 10/19/22	Tue 11/1/22							
233	 Prepare Draft 100% Special Provisions	5 days	Wed 10/5/22	Tue 10/11/22	232,194	Wed 11/2/22	Tue 11/8/22							
234	 QC Draft 100% Special Provisions	5 days	Wed 10/12/22	Tue 10/18/22	233	Wed 11/9/22	Tue 11/15/22							
235	 Address QC Comments	5 days	Wed 10/19/22	Tue 10/25/22	234	Wed 11/16/22	Tue 11/22/22							
236	 WSDOT Review	10 days	Wed 10/26/22	Tue 11/8/22	235	Wed 11/23/22	Tue 12/6/22							
237	 Address WSDOT Comments	10 days	Wed 11/9/22	Tue 11/22/22	236	Wed 12/7/22	Tue 12/20/22							
238	 Submit Proof Copy Special Provisions	0 days	Tue 11/22/22	Tue 11/22/22	237,221	Tue 12/20/22	Tue 12/20/22							
239	 12.2.4 Engineers Cost Estimate	228 days	Fri 1/7/22	Tue 11/22/22		Wed 6/8/22	Tue 12/20/22							
240	 Prepare Draft 60% Cost Estimate	30 days	Fri 1/7/22	Thu 2/17/22	133	Wed 6/8/22	Tue 7/19/22							
241	 QC Draft 60% Cost Estimate	5 days	Fri 2/18/22	Thu 2/24/22	240	Wed 7/20/22	Tue 7/26/22							
242	 Address QC Comments	5 days	Fri 2/25/22	Thu 3/3/22	241	Wed 7/27/22	Tue 8/2/22							
243	 WSDOT Review	10 days	Fri 3/4/22	Thu 3/17/22	242	Wed 8/3/22	Tue 8/16/22							
244	 Address WSDOT Comments	10 days	Fri 3/18/22	Thu 3/31/22	243	Wed 8/17/22	Tue 8/30/22							
245	 Prepare Draft 90% Cost Estimate	20 days	Wed 5/11/22	Tue 6/7/22	244,175	Wed 8/31/22	Tue 9/27/22							
246	 QC Draft 90% Cost Estimate	5 days	Wed 6/8/22	Tue 6/14/22	245	Wed 9/28/22	Tue 10/4/22							
247	 Address QC Comments	5 days	Wed 6/15/22	Tue 6/21/22	246	Wed 10/5/22	Tue 10/11/22							
248	 WSDOT Review	10 days	Wed 6/22/22	Tue 7/5/22	247	Wed 10/12/22	Tue 10/25/22							
249	 Address WSDOT Comments	5 days	Wed 7/6/22	Tue 7/12/22	248	Wed 10/26/22	Tue 11/1/22							
250	 Prepare Draft 100% Cost Estimate	10 days	Wed 10/5/22	Tue 10/18/22	249,194	Wed 11/2/22	Tue 11/15/22							
251	 QC Draft 100% Cost Estimate	5 days	Wed 10/19/22	Tue 10/25/22	250	Wed 11/16/22	Tue 11/22/22							
252	 Address QC Comments	5 days	Wed 10/26/22	Tue 11/1/22	251	Wed 11/23/22	Tue 11/29/22							
253	 WSDOT Review	10 days	Wed 11/2/22	Tue 11/15/22	252	Wed 11/30/22	Tue 12/13/22							
254	 Address WSDOT Comments	5 days	Wed 11/16/22	Tue 11/22/22	253	Wed 12/14/22	Tue 12/20/22							
255	 Submit Final Engineers Estimate	0 days	Tue 11/22/22	Tue 11/22/22	254	Tue 12/20/22	Tue 12/20/22							
256	 12.2.5 Construction Schedule	230 days	Wed 1/19/22	Tue 12/6/22		Wed 5/25/22	Tue 12/20/22							
257	 Develop Draft 60% Construction Schedule	20 days	Wed 1/19/22	Tue 2/15/22	128	Wed 5/25/22	Tue 6/21/22							
258	 QC Draft 60% Construction Schedule	5 days	Wed 2/16/22	Tue 2/22/22	257	Wed 6/22/22	Tue 6/28/22							
259	 Address QC Comments	10 days	Wed 2/23/22	Tue 3/8/22	258	Wed 6/29/22	Tue 7/12/22							
260	 WSDOT Review	10 days	Wed 3/9/22	Tue 3/22/22	259	Wed 7/13/22	Tue 7/26/22							
261	 Address WSDOT Comments	5 days	Wed 3/23/22	Tue 3/29/22	260	Wed 7/27/22	Tue 8/2/22							
262	 Develop Draft 90% Construction Schedule	20 days	Wed 5/11/22	Tue 6/7/22	261,175	Wed 8/3/22	Tue 8/30/22							
263	 QC Draft 90% Construction Schedule	5 days	Wed 6/8/22	Tue 6/14/22	262	Wed 8/31/22	Tue 9/6/22							
264	 Address QC Comments	5 days	Wed 6/15/22	Tue 6/21/22	263	Wed 9/7/22	Tue 9/13/22							
265	 WSDOT Review	20 days	Wed 6/22/22	Tue 7/19/22	264	Wed 9/14/22	Tue 10/11/22							
266	 Address WSDOT Comments	5 days	Wed 7/20/22	Tue 7/26/22	265	Wed 10/12/22	Tue 10/18/22							
267	 Develop Draft 100% Construction Schedule	20 days	Wed 10/5/22	Tue 11/1/22	266,194	Wed 10/19/22	Tue 11/15/22							
268	 QC Draft 100% Construction Schedule	5 days	Wed 11/2/22	Tue 11/8/22	267	Wed 11/16/22	Tue 11/22/22							
269	 Address QC Comments	5 days	Wed 11/9/22	Tue 11/15/22	268	Wed 11/23/22	Tue 11/29/22							
270	 WSDOT Review	10 days	Wed 11/16/22	Tue 11/29/22	269	Wed 11/30/22	Tue 12/13/22							
271	 Address WSDOT Comments	5 days	Wed 11/30/22	Tue 12/6/22	270	Wed 12/14/22	Tue 12/20/22							
272	 Submit Final Construction Schedule	0 days	Tue 12/6/22	Tue 12/6/22	271	Tue 12/20/22	Tue 12/20/22							
273	 Project Ad Ready	0 days	Tue 12/20/22	Tue 12/20/22	15,23,28,32,36,44,49,58,60,70,75	Tue 12/20/22	Tue 12/20/22							

WSDOT SR 526 Corridor Improvements
 Phase 2a Preliminary Schedule Geometric Design
 September 22, 2020




<p>WSDOT SR 526 Corridor Improvements Phase 2a Preliminary Schedule Geometric Design September 22, 2020</p>


Nov



<p>WSDOT SR 526 Corridor Improvements Phase 2a Preliminary Schedule Geometric Design September 22, 2020</p>




WSDOT SR 526 Corridor Improvements
Phase 2a Preliminary Schedule Geometric Design
September 22, 2020

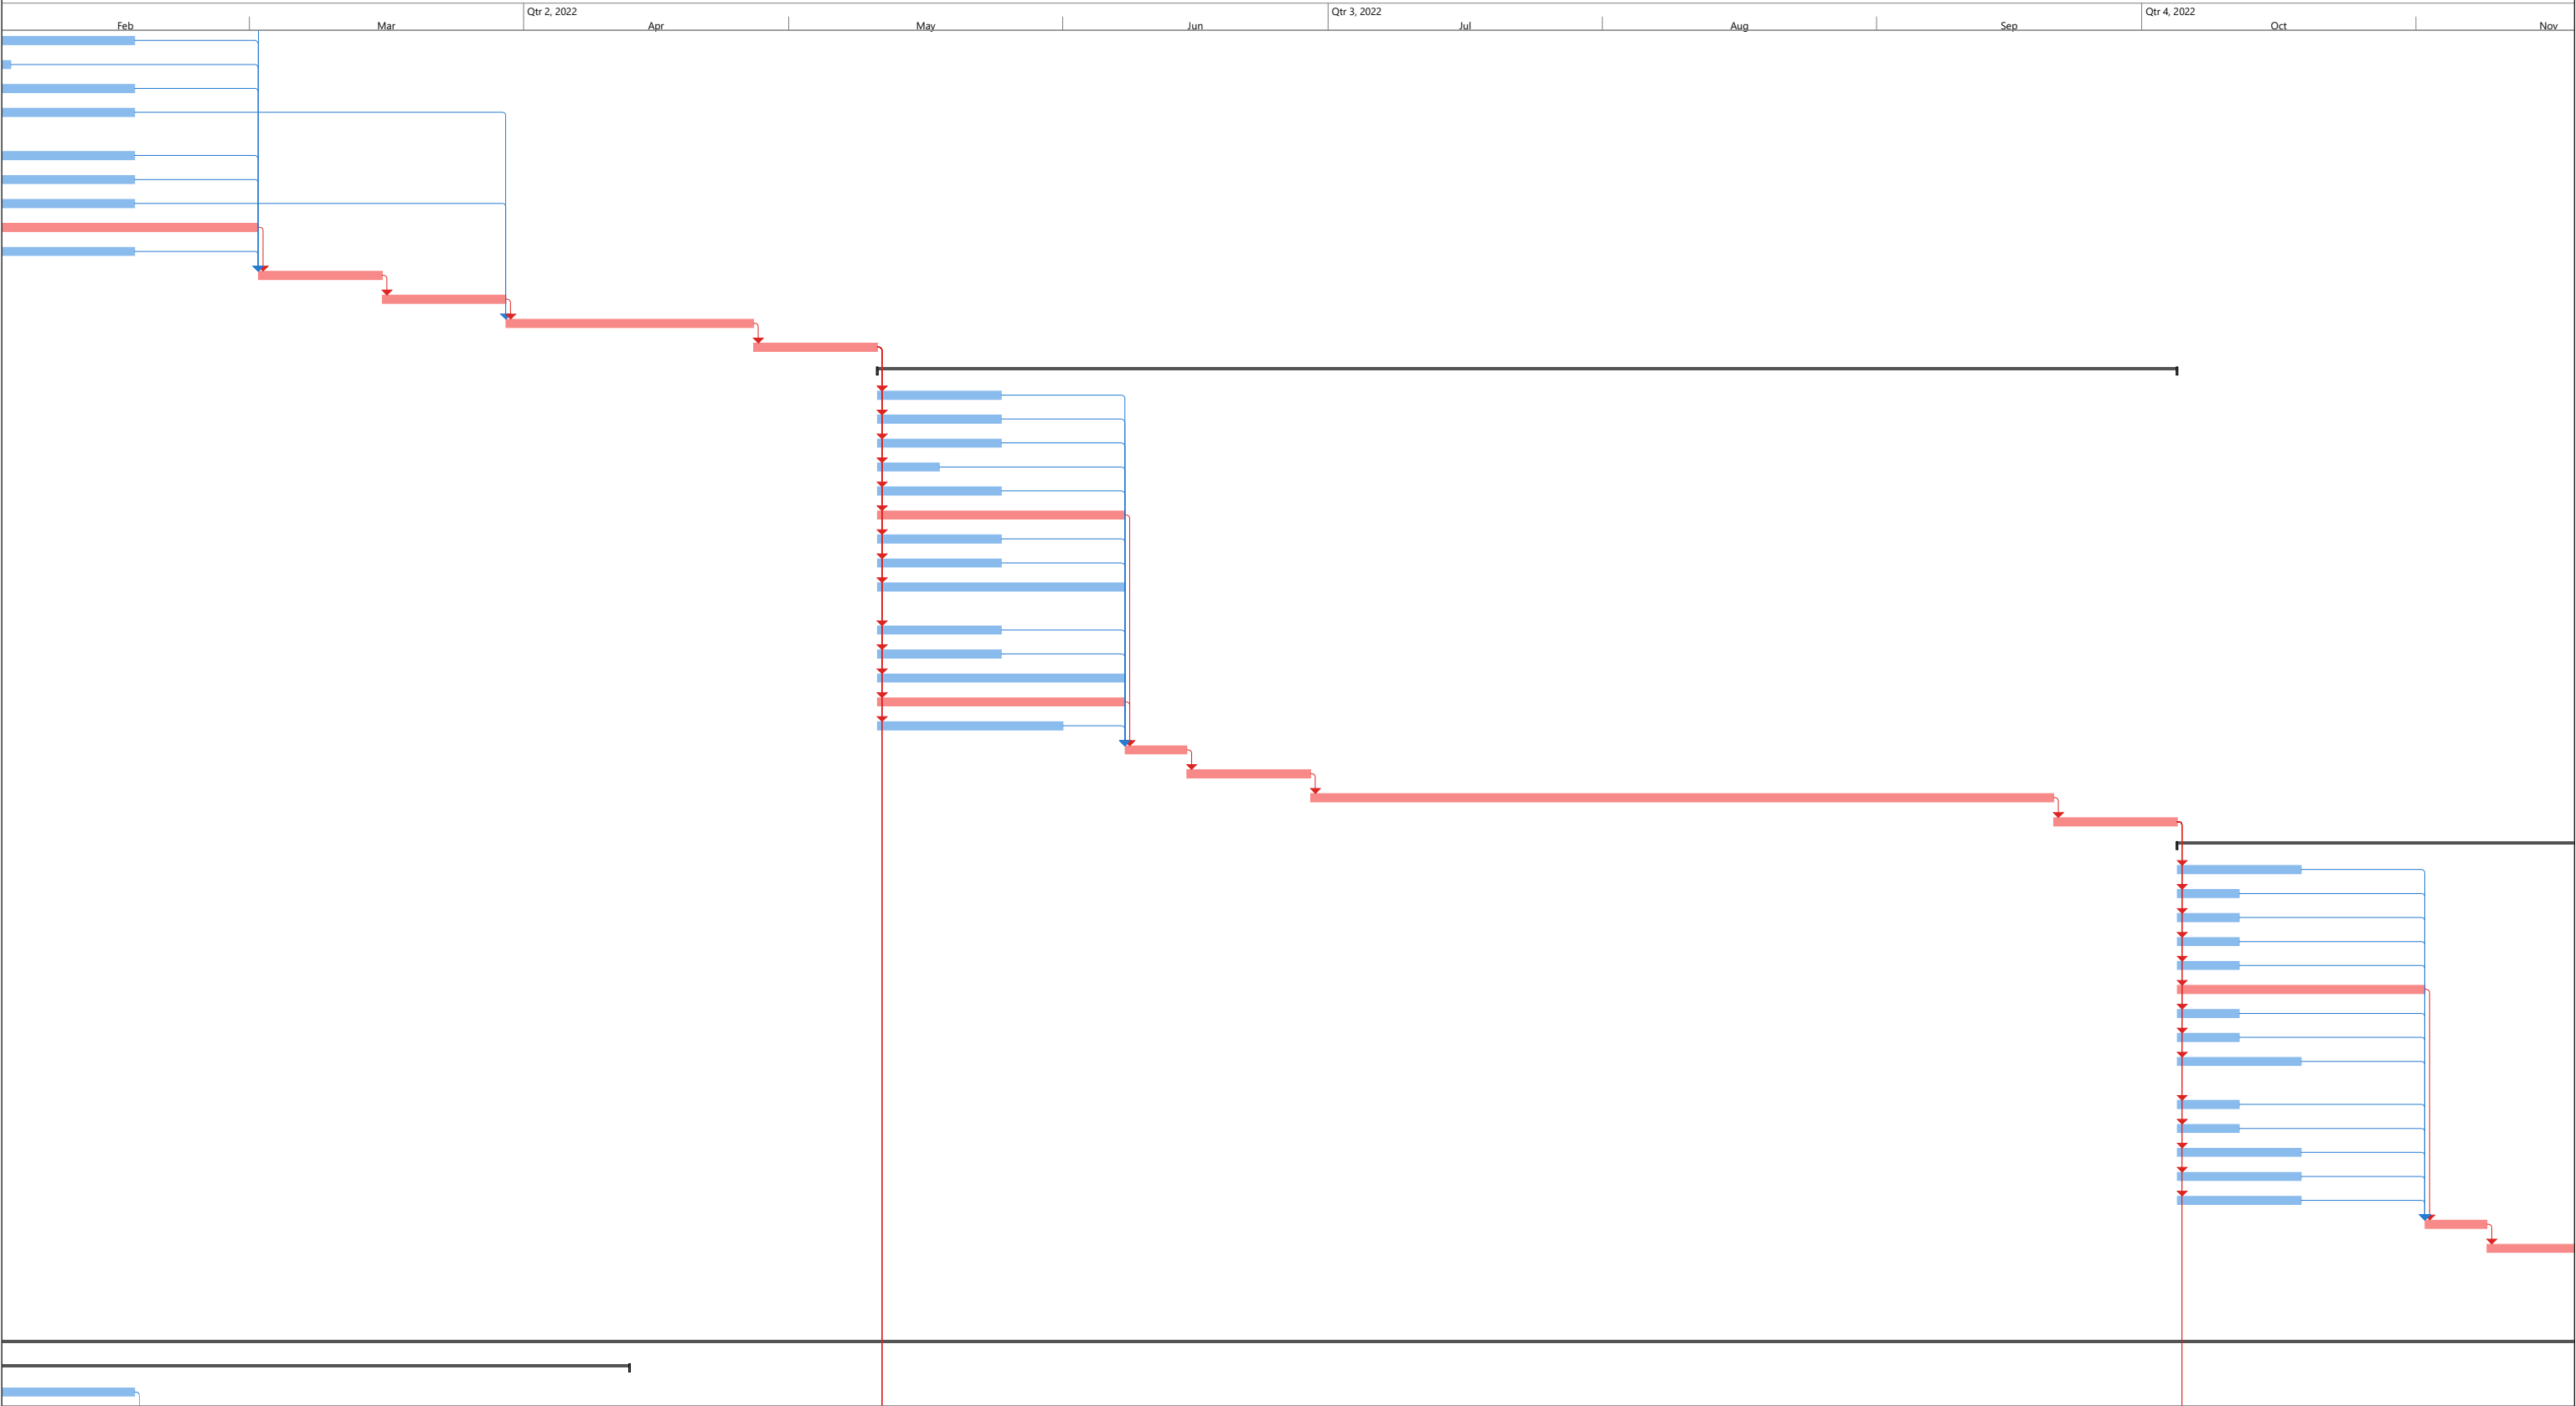

Project: SR 526 Phase 2 Schedu Date: Wed 12/29/21	Task	<div></div> Summary	<div></div> Inactive Milestone	<div></div> Duration-only	<div></div> Start-only	<div></div> External Milestone	<div></div> Critical Split	<div></div>
	Split	<div></div> Project Summary	<div></div> Inactive Summary	<div></div> Manual Summary Rollup	<div></div> Finish-only	<div></div> Deadline	<div></div> Progress	<div></div>
	Milestone	<div></div> Inactive Task	<div></div> Manual Task	<div></div> Manual Summary	<div></div> External Tasks	<div></div> Critical	<div></div> Manual Progress	<div></div>

<p>WSDOT SR 526 Corridor Improvements Phase 2a Preliminary Schedule Geometric Design September 22, 2020</p>

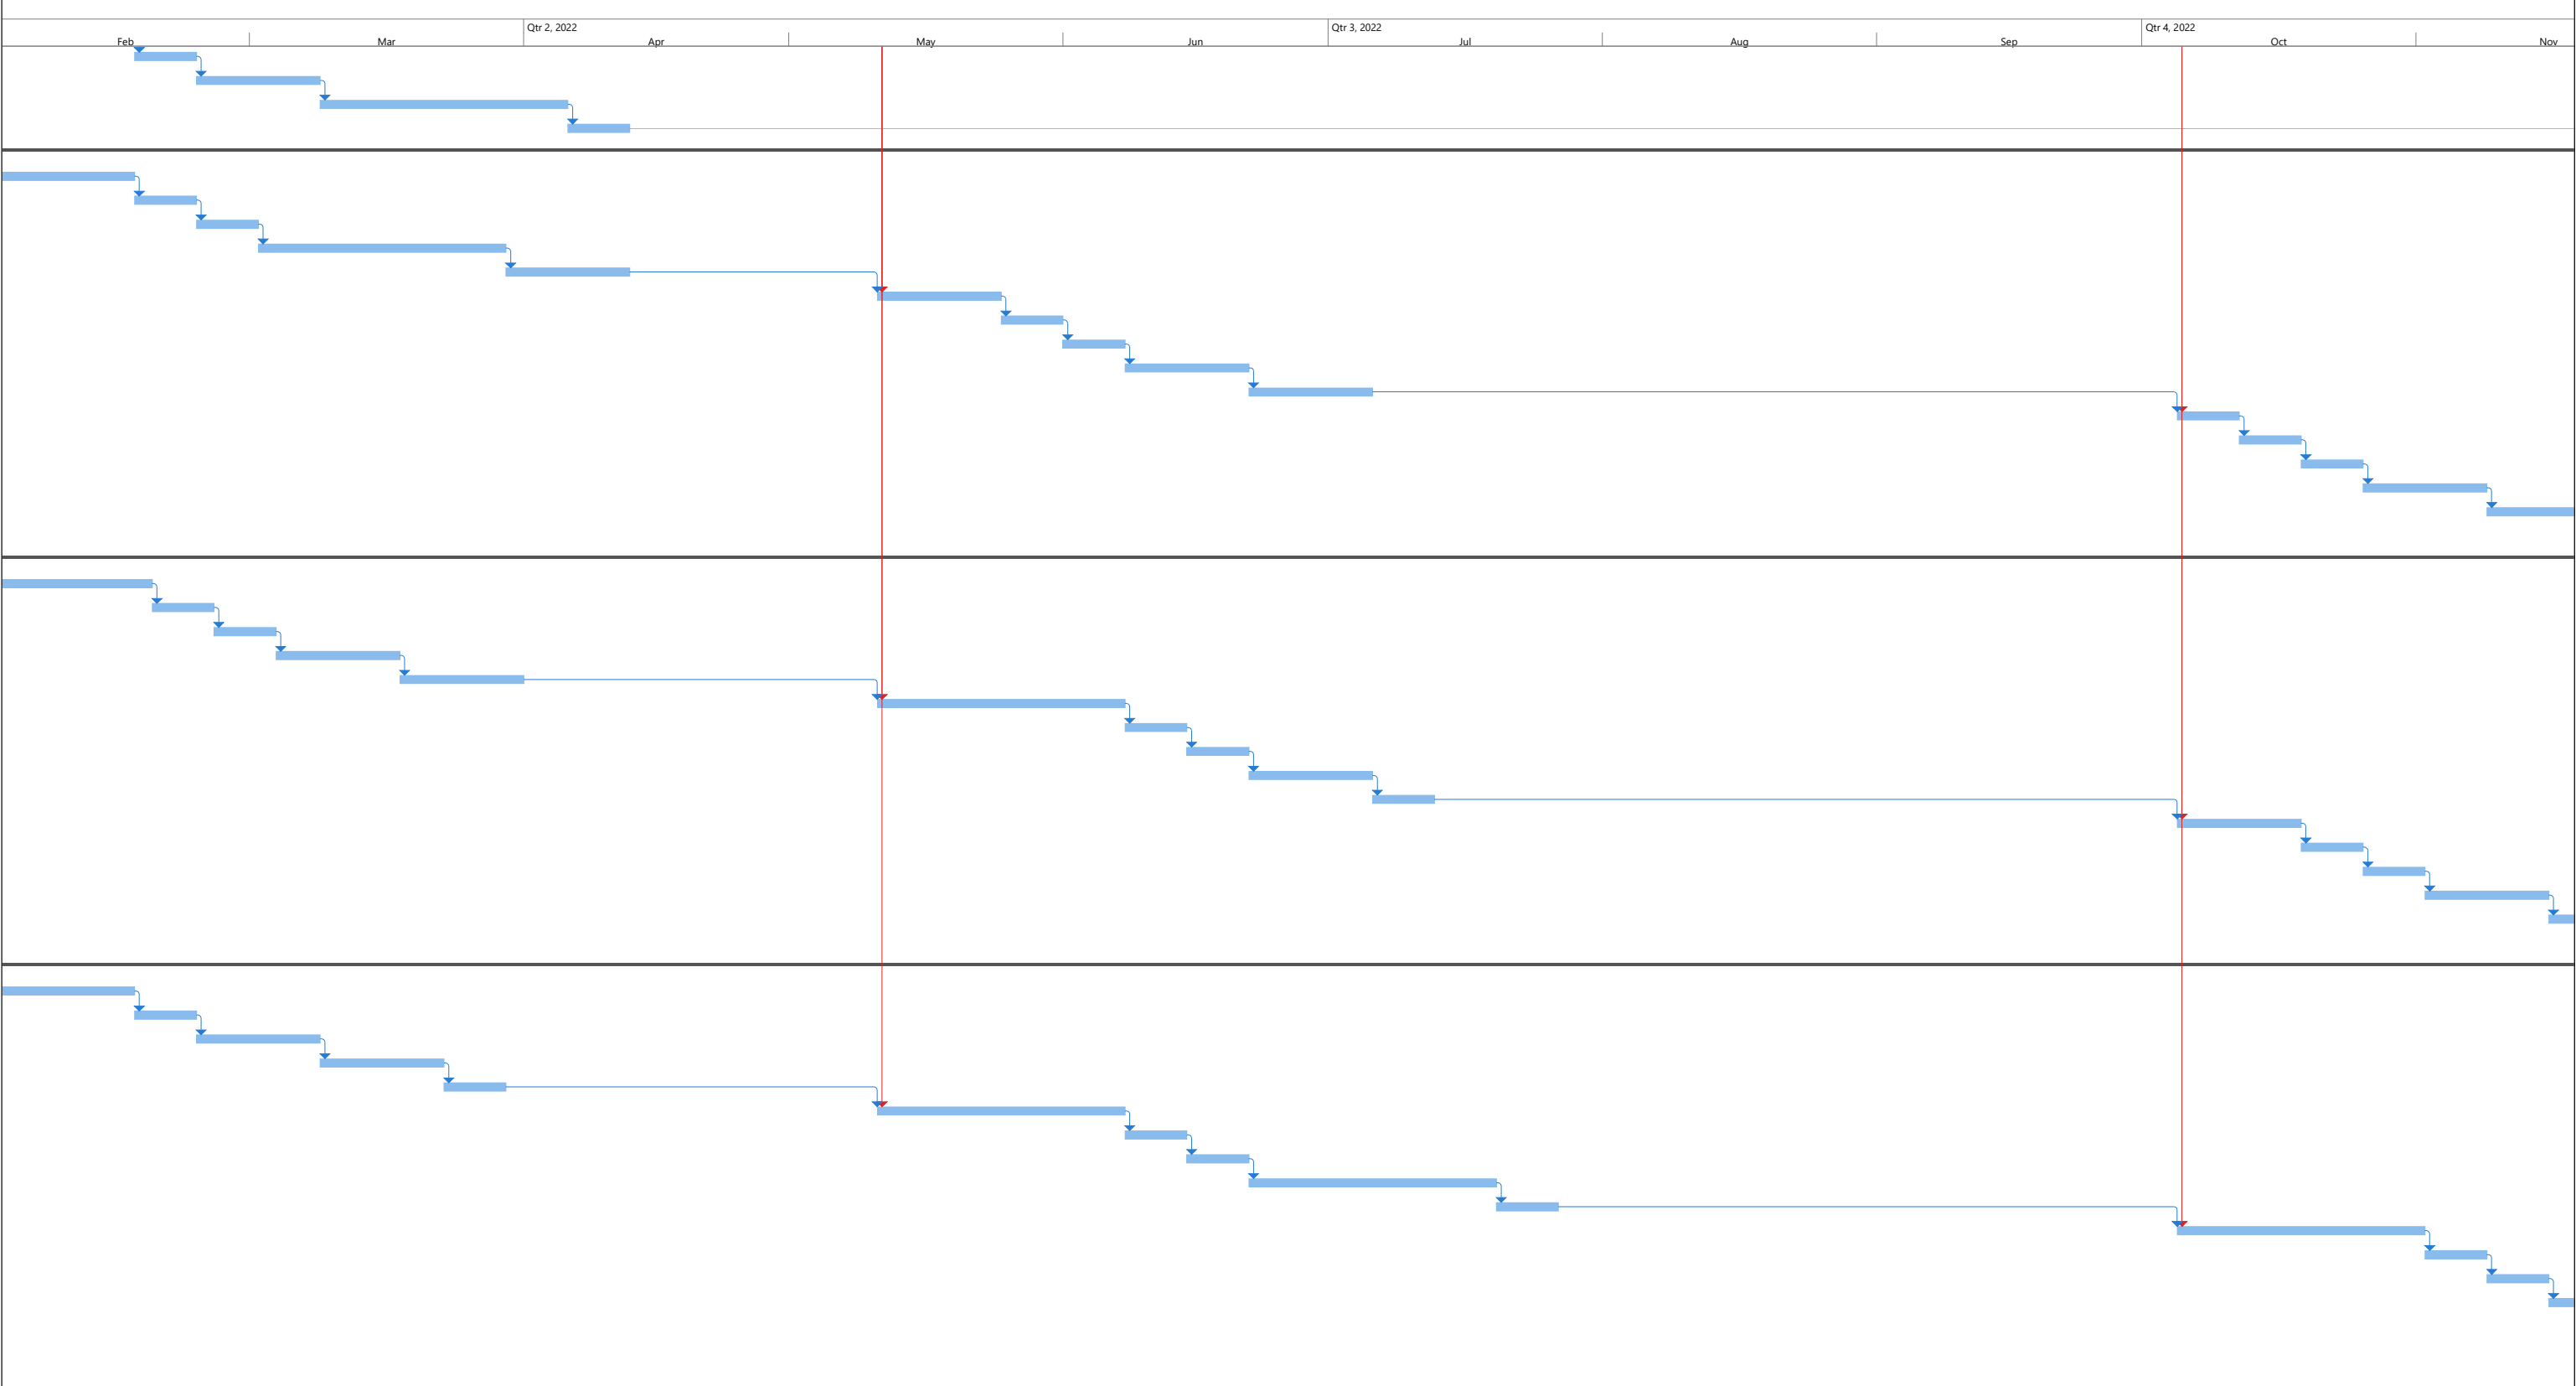

WSDOT SR 526 Corridor Improvements
Phase 2a Preliminary Schedule Geometric Design
September 22, 2020

2023		2022	
Qtr 1, 2023	Qtr 2, 2023	Qtr 1, 2022	Qtr 2, 2022
1	2	3	4

Dec

Jan

Feb

Mar


Apr


May

Jun

Jul

Aug





WSDOT SR 526 Corridor Improvements
Phase 2a Preliminary Schedule Geometric Design
September 22, 2020

2023

Qtr 1, 2023

Nov

Dec

Jan

Feb

Mar

Qtr 2, 2023

Apr


May

Jun

Qtr 3, 2023

Jul

Aug

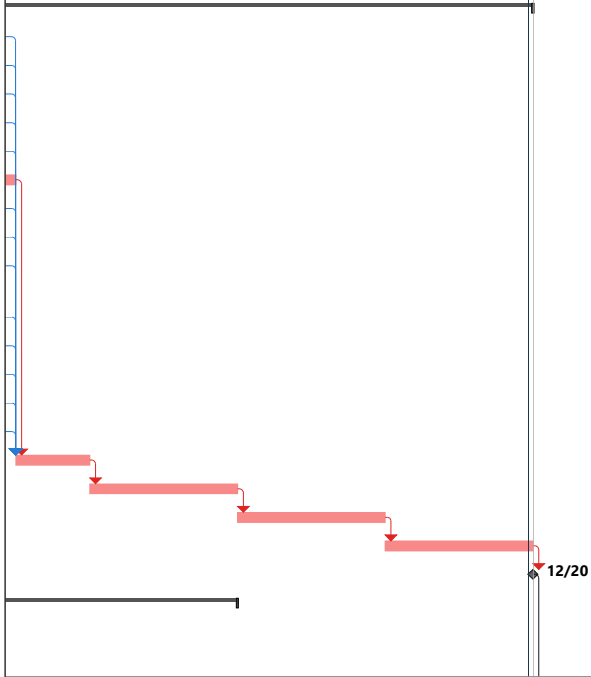

Project: SR 526 Phase 2 Schedu
Date: Wed 12/29/21

Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split
Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress
Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress

WSDOT SR 526 Corridor Improvements
Phase 2a Preliminary Schedule Geometric Design
September 22, 2020



Project: SR 526 Phase 2 Schedu Date: Wed 12/29/21	Task	Summary	Inactive Milestone	Duration-only	Start-only	External Milestone	Critical Split	
	Split	Project Summary	Inactive Summary	Manual Summary Rollup	Finish-only	Deadline	Progress	
	Milestone	Inactive Task	Manual Task	Manual Summary	External Tasks	Critical	Manual Progress	
