BLAST REPORT **BLAST REPORT #** P004

☐ Sanders Construction, Inc. ☐ Western States Drilling & Blasting, Inc.

DATE: 23RD. SEP/10 EXACT TIME OF SHOT: 6:39 P.M.

CUSTOMER: KLB JOB NO.: WS 21005

SHOT LOCATION WITH GPS COORDINATES: STA 1334 TICKET NO.:

ON FREE FACE ADJACENT TO I-90 CHECK LIST COMPLETED: YES NO

TYPE OF ROCK: LAPILLI TUFF FACE HEIGHT: 4-7' FT. POUNDS PER DELAY: 1.92

TOTAL HOLES: 14

NUMBER OF HOLES: 14 HOLE DIA: 1 5/8" BxS 3.5 x 3.5 STEMMING: 1/2" CRUSH DEPTH: VARIOUS

NUMBER OF HOLES: HOLE DIA: BxS x STEMMING: DEPTH:

POWDER FACTOR: LBS. OF EXPLOSIVES: 26.875 YARDS OF ROCK: 148 YRDS

WEATHER: RAIN WIND: CALM.

EXACT MONITOR LOCATION(GPS): DIRECTION OF BLAST: MONITOR TYPE:

MONITOR: L/R T V PVS Db MONITOR SERIAL NO.:

DISTANCE TO BLAST: AVERAGE POUNDS PER HOLE: OPERATOR:

EXACT MONITOR LOCATION(GPS): DIRECTION OF BLAST: MONITOR TYPE:

MONITOR: L/R T V PVS Db MONITOR SERIAL NO.:

DISTANCE TO BLAST: AVERAGE POUNDS PER HOLE: OPERATOR:

EXPLOSIVES

DESCRIPTION	QUANTITY USED	DATE CODE	MAGAZINE	REMOVED	RETURNED
LOCATION:					
BULK A/N	Lbs				
BAG ANFO	Bags				
POWDER 1 1/4" POWERDITCH	43 STICKS ea.	07JY10J1		91	48
POWDER 1000	ea.				
lb. BOOSTER	ea.				
lb. BOOSTER	ea.				
16 ft. HANDIDETS	14 UNITS ea.	190C09B4		36	22
ft.	ea.				
ft.	ea.				
ft.	ea.				
12 ft. 17MS HTD'S	4 ea.	14JY08B4		5	1
ft.	ea.				
ft. ms	ea.				
	ft.				
GRAIN CORD	ft.				
GRAIN CORD	ft.				
MISCELLANEOUS					

COMMENTS:

BLASTER'S SIGNATURE: [signature] LICENSE NO.: UP21262

B GREEN

Revised 03/04 **ATTACH SKETCH OF SHOT** THIS FORM MUST BE FILLED OUT COMPLETELY

COMPUTATIONS

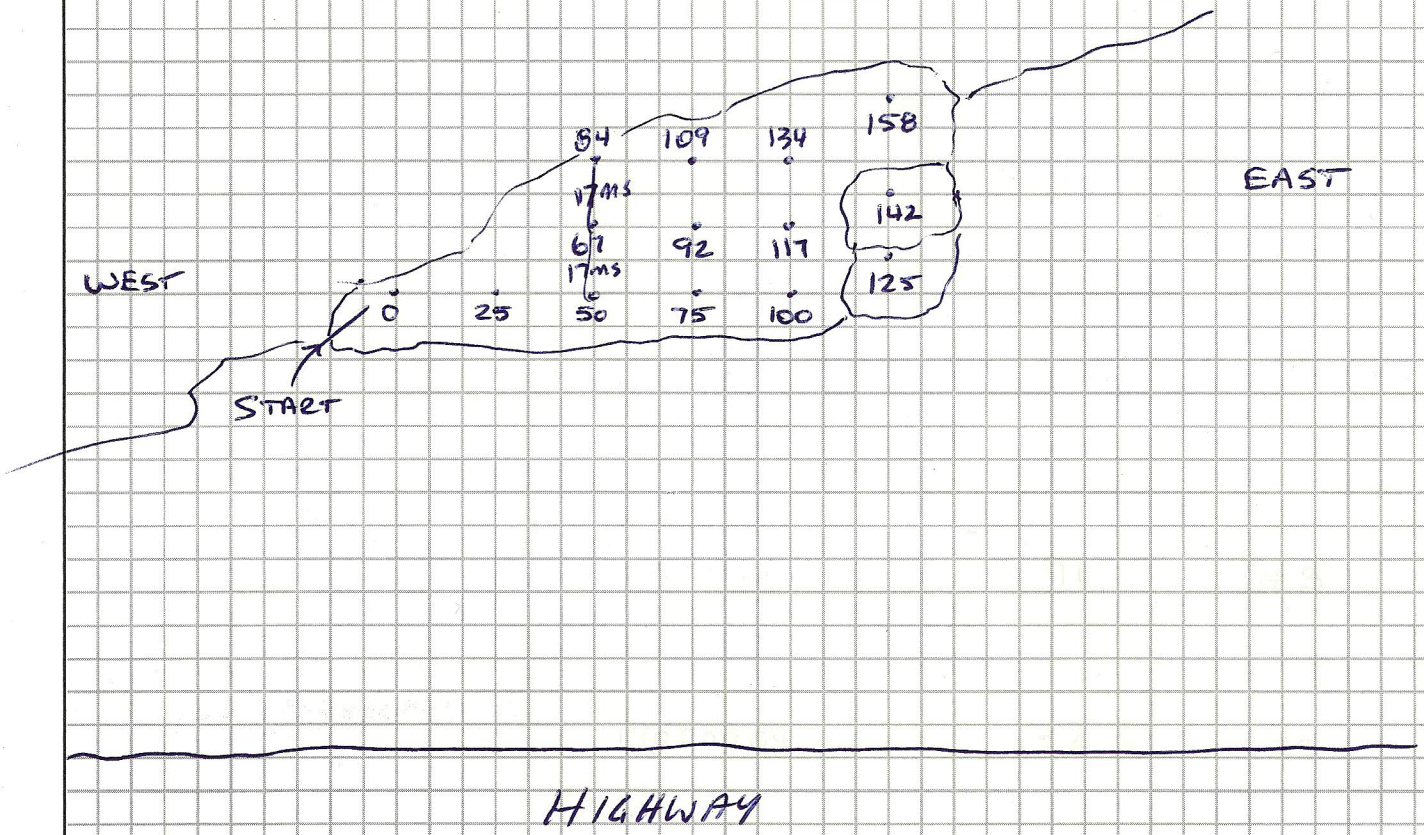

PACIFIC BLASTER: B Green

PACIFIC BLASTING & DEMOLITION LTD. 3183 NORLAND AVENUE BURNABY, BC V5B 3A9 TEL 604 291 1255 FAX 604 291 2813 (INSURED AND BONDED)	JOB. NO. WS 21005 SUPT.
	PROJECT HYAK TO SNOWSHED I-90.
	LOCATION STA 1334
	DETAILS BLAST # P004
